



This is a digital copy of a book that was preserved for generations on library shelves before it was carefully scanned by Google as part of a project to make the world's books discoverable online.

It has survived long enough for the copyright to expire and the book to enter the public domain. A public domain book is one that was never subject to copyright or whose legal copyright term has expired. Whether a book is in the public domain may vary country to country. Public domain books are our gateways to the past, representing a wealth of history, culture and knowledge that's often difficult to discover.

Marks, notations and other marginalia present in the original volume will appear in this file - a reminder of this book's long journey from the publisher to a library and finally to you.

Usage guidelines

Google is proud to partner with libraries to digitize public domain materials and make them widely accessible. Public domain books belong to the public and we are merely their custodians. Nevertheless, this work is expensive, so in order to keep providing this resource, we have taken steps to prevent abuse by commercial parties, including placing technical restrictions on automated querying.

We also ask that you:

- + *Make non-commercial use of the files* We designed Google Book Search for use by individuals, and we request that you use these files for personal, non-commercial purposes.
- + *Refrain from automated querying* Do not send automated queries of any sort to Google's system: If you are conducting research on machine translation, optical character recognition or other areas where access to a large amount of text is helpful, please contact us. We encourage the use of public domain materials for these purposes and may be able to help.
- + *Maintain attribution* The Google "watermark" you see on each file is essential for informing people about this project and helping them find additional materials through Google Book Search. Please do not remove it.
- + *Keep it legal* Whatever your use, remember that you are responsible for ensuring that what you are doing is legal. Do not assume that just because we believe a book is in the public domain for users in the United States, that the work is also in the public domain for users in other countries. Whether a book is still in copyright varies from country to country, and we can't offer guidance on whether any specific use of any specific book is allowed. Please do not assume that a book's appearance in Google Book Search means it can be used in any manner anywhere in the world. Copyright infringement liability can be quite severe.

About Google Book Search

Google's mission is to organize the world's information and to make it universally accessible and useful. Google Book Search helps readers discover the world's books while helping authors and publishers reach new audiences. You can search through the full text of this book on the web at <http://books.google.com/>



TA
24
N7A5

UC-NRLF



\$B 113 896

YC104853

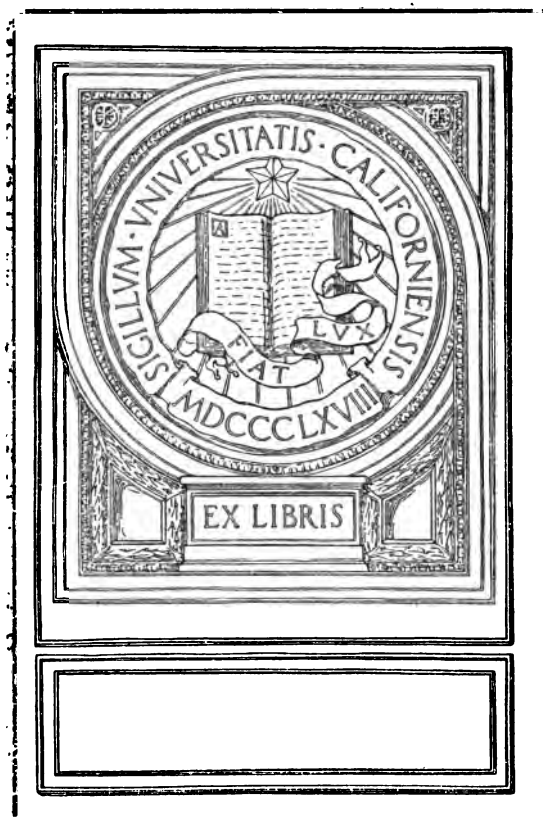

P.C. New York (state) Reconstruction Commission

STATE OF NEW YORK
EXECUTIVE CHAMBER

REPORT OF RECONSTRUCTION COMMISSION


ON

Public Improvements in Progress, Not
Started and Contemplated

CITIES

UNIV. OF
CALIFORNIA

APRIL 14, 1919



ALBANY
J. B. LYON COMPANY, PRINTERS
1919

TA24
N7A5

CITIES

RECAPITULATION — FOR DETAILS, SEE FOLLOWING PAGES

EXCEPTING NEW YORK CITY, WHICH IS ON A SEPARATE SHEET

CITY	WORK IN PROGRESS		WORK NOT STARTED		WORK CONTEMPLATED
	Moneys Available	Estimated Cost of Construction	Moneys Available	Estimated Cost of Construction	Estimated Cost of Construction
Albany	\$174,447	\$164,447	\$443,000	\$690,000	\$418,040
Amsterdam			55,000	55,000
Auburn			6,000	6,000	123,000
Batavia
Beacon
Buffalo
Binghamton	75,000		60,000	60,000	225,000
Canandaigua
Cortland			11,830	10,250	2,250
Cohoes			370,000	370,000
Corning
Dunkirk	27,845	27,845	26,668	26,668
Elmira			102,000		250,000
Fulton
Glen Cove
Geneva
Gloversville					71,000
Glens Falls
Hudson
Hornell
Ithaca			107,500	92,500
Jamestown	142,953	142,953			5,628
Johnstown
Kingston			165,000	165,000
Little Falls					100,000
Lockport					223,500
Lackawanna	700	700	8,000	8,000
Mechanicville					200,000
Middletown					460,000
Mt. Vernon					198,000
Niagara Falls			201,205	198,105	659,800

CITIES —Continued

CITY	WORK IN PROGRESS		WORK NOT STARTED		WORK CONTEMPLATED
	Moneys Available	Estimated Cost of Construction	Moneys Available	Estimated Cost of Construction	Estimated Cost of Construction
Norwich					
No. Tonawanda ..			\$80,000	\$77,000	
Newburgh					\$525,000
New Rochelle	\$150,000	\$160,000			100,000
Olean					131,700
Oneida			81,773	77,343	
Oneonta			1,200	1,200	82,845
Ogdensburg	9,000	9,000			50,000
Oswego	500,000	500,000			175,000
Poughkeepsie	37,000	37,000	43,400	43,400	
Plattsburg					25,000
Pt. Jervis					
Rochester	546,000	493,000	986,000	986,000	2,300,600
Rome			56,000	56,000	125,000
Rensselaer					131,600
Schenectady			72,000	72,000	70,265
Sherrill			1,600	1,600	
Saratoga					14,460
Syracuse	634,000	1,288,500	733,620	1,748,770	158,800
Salamanca					55,000
Troy			227,000	227,000	
Tonawanda	111,000	106,000	8,000	7,000	50,000
Utica			180,000	180,000	30,000
Watervliet					
Watertown	20,000	20,000	290,000	550,000	60,000
White Plains	14,700	14,700	51,000	71,075	
Yonkers	69,130	69,130			35,000
	<u>\$2,511,775</u>	<u>\$3,033,275</u>	<u>\$4,367,796</u>	<u>\$5,779,911</u>	<u>\$7,055,998</u>
Grand totals			<u>Amount Available</u>	<u>Estimated Cost</u>	
			\$6,879,571	\$15,869,174	

989965

CITIES — **WORK IN**

City	Nature of Work	Location
Albany	Grading and vitrified pipe sewer	Quail st., Livingston ave. to Manning boulevard
Albany	Parking city property — grading, sodding, concrete walks, etc.	Pine, Lodge, Steuben and Eagle sts.
Albany	Asphalt paving, concrete curbing and walks	Euclid and Lenox aves.
Albany	Asphalt paving, concrete curbing and walks	Homestead ave., from Melrose to Washington ave.
Albany	Asphalt paving, concrete curbing and walks	Catherine st., Dove st. to Delaware ave.
Albany	Brick and asphalt paving, granite curbing, concrete walks, and vitrified pipe sewers	Banker, Mercer, Peyster and Warren sts., and Main, Park and Ryckman aves.
Amsterdam
Auburn
Batavia
Beacon
Buffalo
Binghamton ..	Intercepting sewer — concrete, cast iron and tile	Parks of Chenango and Susquehanna rivers
Canandaigua
Cortland
Cohoes
Corning
Dunkirk	Sanitary sewer	Seal st.
Dunkirk	Slag road	Light st.
Dunkirk	Highway	Roberts rd.
Dunkirk	Concrete pavement	East Lake rd.
Elmira
Fulton
Glen Cove
Geneva
Gloversville

Continued

PROGRESS

Moneys Available	Estimated Cost of Construction	Date Work Will Start	Estimated Date of Completion	Contract or Force Account	Remarks
\$14,000	\$4,000	April, 1919	20 days	Contract	
2,800	2,800	April, 1919	15 days	Contract	
20,071	20,071	June, 1919	20 days	Contract	
25,015	25,015	July, 1919	30 days	Contract	
9,061	9,061	July, 1919	40 days	Contract	
103,500	103,500	July, 1919	90 days	Contract	
<u>\$174,447</u>	<u>\$164,447</u>				
.....				
.....				
.....				
.....				
\$75,000	May 15, '19	Contract	Contractor has applied to the city for relief from his contract
.....				
.....				
.....				
\$500	\$500	May 1, '19	12 days	Force	
4,639	4,639	Apr. 8, '19	25 days	Contract	
3,206	3,206	May 1, '19	60 days	Contract	
19,500	19,500	60 days	Contract.	This work will start as soon as adjustment of traction matters is made.
<u>\$27,845</u>	<u>\$27,845</u>				
.....				
.....				
.....				
.....				

CITIES —
WORK IN PROG

City	Nature of Work	Location
Glens Falls
Hudson
Hornell
Ithaca
Jamestown ..	Shale brick pavement	Eleven streets
Johnstown
Kingston
Little Falls
Lockport
Lackawanna ..	Sanitary sewer	Gibbons st.
Mechanicville
Middletown
Mt. Vernon
Niagara Falls
Norwich
No. Tonawanda
Newburgh
New Rochelle ..	Roads	All over city
Olean
Oneida
Oneonta
Ogdensburg ..	Concrete market building....	Isabella st.
Oswego	Hydro-electric power house..	Dam No. 6.....
Poughkeepsie ..	Grading street, retaining wall, etc.	Brookside ave. extension....
Poughkeepsie ..	Pre-filter at water works....	City water plant
Plattsburg
Port Jervis
Rochester	Bath house	Durand Eastman park.....
Rochester	Bridge	Clarissa st. over Genesee river.
Rochester	Asphalt pavement	Genesee Park boulevard....
Rochester	Vitrified pipe sewer.....	Randolph st. outlet.....
Rochester	Addition to School No. 27...	Central park and First st....
Rochester	Jefferson, Jr., High School...	Exposition park
Rome
Rensselaer
Schenectady
Sherrill
Saratoga
Syracuse	School house	17th ward, Madison school...
Syracuse	School house	9th ward, Porter school....
Syracuse	Garbage reduction plant....	Hiawatha st.
Syracuse	Sewer	Teall ave. and Manlius st....
Syracuse	Sewer	Part 1 of 17th ward.....
Syracuse	Sewer	Part 2 of 17th ward.....

*Continued***RESS — Continued**

Moneys Available	Estimated Cost of Construction	Date Work Will Start	Estimated Date of Completion	Contract or Force Account	Remarks
.....				
.....				
.....				
\$142,953	\$142,953				
.....				
.....				
.....				
700	700	March 15	April 15	Contract	
.....				
.....				
.....				
.....				
150,000	160,000	At once	All year	Contract and Force	
.....				
.....				
9,000	9,000		1 to 2 mos.	Contract	
500,000	500,000	Sum. '19	2 years	Contract	Private interests have caused sus- pension of work.
7,000	7,000	March 17	60 days	Contract and Force	
30,000	30,000	April 15	70 days	Contract	
<u>\$37,000</u>	<u>\$37,000</u>				
.....				
.....				
\$70,000	\$70,000	Underway	150 days	Contract	
150,000	150,000	Underway	200 days	Contract	
105,000	39,600	April 1	90 days	Contract	
.....	13,000	Underway	35 days	Contract	
42,000	42,000	May 1	Contract	
179,000	179,000	Underway	Oct. 1	Contract	
<u>\$546,000</u>	<u>\$493,000</u>				
.....				
.....				
.....				
.....				
.....				
\$57,000	\$212,000	Underway	400 days	Contract	
75,000	225,000	Underway	400 days	Contract	
250,000	250,000	Underway	200 days	Contract	
22,000	15,000	Underway	60 days	Contract	
15,000	4,000	Underway	60 days	Contract	
20,000	8,000	Underway	60 days	Contract	

**CITIES —
WORK IN PROG**

City	Nature of Work	Location
Syracuse	Sewer	Part 3 of 17th ward.....
Syracuse	Sewer	Part of east section, 17th wd.
Syracuse	Creek improvement and sewer.	Along Onondaga creek.....
Salamanca
Troy
Tonawanda ...	48" iron and wood pipe intake.	Pumping station to intake pier in Niagara river.....
Utica
Watervliet
Watertown ...	Macadam roads	City streets
White Plains .	Sanitary sewer	Thompson ave.
White Plains .	Bluestone curb and brick gutter	Winchester st.
Yonkers	Sewer	Kimball ave.
Yonkers	Sewer	Scott ave.
Yonkers	Sewer	Hyatt ave.
Yonkers	Grading	Kimball ave.
Yonkers	Grading	Fortfield ave.
Yonkers	Sewer	Allison ave.
Yonkers	Grading	Central Park ave.....

GRAND TOTAL

*Continued***RESS — Concluded**

Moneys Available	Estimated Cost of Construction	Date Work Will Start	Estimated Date of Completion	Contract or Force Account	Remarks
\$5,000	\$1,500	Underway	30 days	Contract	
37,000	30,000	Underway	60 days	Contract	
153,000	543,000	April 1	750 days	Contract	
<u>\$634,000</u>	<u>\$1,288,500</u>				
.....				
.....				
\$111,000	\$106,000	Started	5 mo.	Contract	
.....				
.....				
20,000	20,000	May 15	120 days		
12,000	12,000	April 1	90 days	Contract	
2,700	2,700	April 1	30 days	Contract	
<u>\$14,700</u>	<u>\$14,700</u>				
\$6,064	\$6,064	Uncert'n	Uncert'n	Contract	Contractor claims work is unprof- itable. Matter under advisement.
1,112	1,112	Uncert'n	Uncert'n	Contract	(Same as above)
2,643	2,643	Uncert'n	Uncert'n	Contract	(Same as above)
14,616	14,616	Uncert'n	Uncert'n	Contract	(Same as above)
12,750	12,750	Uncert'n	Uncert'n	Contract	(Same as above)
4,428	4,428	Uncert'n	Uncert'n	Contract	(Same as above)
27,517	27,517	April 1	Sept. 1	Contract	
<u>\$69,130</u>	<u>\$69,130</u>				
<u>\$2,511,775</u>	<u>\$3,033,275</u>				

**CITIES —
WORK NOT**

City	Nature of Work	Location
Albany	Concrete trunk sewer.....	Tivoli st.....
Albany	Swimming pool, walks, etc...	Lincoln park.....
Albany	Concrete dock walls, parking, granite block pavements, etc.	Madison ave. to Westerlo st..
Albany	Brick highway.....	Lawn st.....
Albany	Asphalt highway.....	Rensselaer ave.....
Albany	Asphalt highway.....	Mapleridge ave.....
Albany	Asphalt street, curbing and walks	Ridgefield st.....
Albany	Brick pavement, curb and walks	North st.....
Albany	Municipal bldg. for police headquarters	Eagle and Beaver sts.....
Albany	Brick school house.....	New Scotland ave.....
Albany	Brick school house.....	Whitehall road.....
Amsterdam ...	Extension of water mains... ..	
Amsterdam ..	Pavements	East Main st.....
Amsterdam ...	Sewers	
Auburn	Sewage disposal plant.....	York and Division sts.....
Batavia	
Beacon	
Buffalo	
Binghamton ..	Tile sewers.....	Various parts of city.....
Canandaigua	

Continued

STARTED

Moneys Available	Estimated Cost of Construction	Date Work Will Start	Estimated Date of Completion	Contract or Force Account	Remarks
.....	Cost to be assessed — Not estimated.
\$20,000	\$20,000	Contract & Force	
180,000	180,000	Property to be acquired or condemned.
18,000	18,000	June	40 days	Contract	
15,000	15,000	June	30 days	Contract	
.....	May	30 days	Contract	Cost to be assessed — Not estimated.
.....	May	30 days	Contract	Cost to be assessed — Not estimated.
.....	July	25 days	Contract	Cost to be assessed — Not estimated.
110,000	207,000	Year 1919	Additional appropriations or lower costs for materials and labor.
50,000	125,000	Year 1919	150 days	Additional appropriations or lower costs for materials and labor.
50,000	125,000	Year 1920	150 days	Contract	
<u>\$443,000</u>	<u>\$690,000</u>				
\$15,000	\$15,000	
30,000	30,000	July 1	90 days	Contract	
10,000	10,000	
<u>\$55,000</u>	<u>\$55,000</u>				
\$6,000	\$6,000	May 1	50 days	Contract	
.....	
.....	
60,000	60,000	May 1	180 days	Contract	
.....	

CITIES — WORK NOT STAR

City	Nature of Work	Location
Cortland	Resurfacing streets with slag.	Port Watson, Tompkins st., and Groton ave.....
Cohoes	New high school.....
Cohoes	Paving streets.....
Corning
Dunkirk	Highways (asphalt).....
Dunkirk	Highway	Leopard st.....
Dunkirk	Highway	Lark st.....
Elmira	Reinforced concrete bridges and retaining walls.....
Elmira	Pavements
Elmira	Tile sewers.....
Fulton
Glen Cove
Geneva
Gloversville
Glens Falls.....
Hudson
Hornell
Ithaca	Brick and bitulithic pave- ments	Various streets.....
Ithaca	Sanitary sewer extension...	South Aurora and Hector sts.
Ithaca	Storm sewers.....	No. Tioga and No. Aurora sts.
Ithaca	Water main extensions.....	So. Aurora and Hector sts...
Jamestown
Johnstown
Kingston	Street, park and play ground work
Little Falls
Lockport
Lackawanna ..	Macadam streets.....
Mechanicville
Middletown
Mt. Vernon
Niagara Falls.	Wading place and swimming pool
Niagara Falls .	Sewers
Niagara Falls.	Improvements at city market.
Niagara Falls.	Repaving	Pine ave., Sugar st. to city line

Continued

TED — Continued

Moneys Available	Estimated Cost of Construction	Date Work Will Start	Estimated Date of Completion	Contract or Force Account	Remarks
\$11,830	\$10,250	May 1	Aug. 1	Force	
270,000	270,000	
100,000	100,000	
<u>\$370,000</u>	<u>\$370,000</u>				
.....	
\$11,500	\$11,500	May 15	60 days	Force	
4,966	4,966	30 days	Contract	
10,202	10,202	May 1	60 days	Contract	
<u>\$26,668</u>	<u>\$26,668</u>				
.....	
\$8,000	Contract	
90,000	Contract	
4,000	Contract	
<u>\$102,000</u>	<u>.....</u>				
.....	
.....	
.....	
.....	
.....	
.....	
\$100,000	\$85,000	April 15	Sept. 1	Contract	
3,000	3,000	April 1	June 1	Force	
2,000	2,000	May 1	June 15	Force	
2,500	2,500	March 17	May 1	Force	
<u>\$107,500</u>	<u>\$92,500</u>				
.....	
.....	
\$165,000	\$165,000	Force	
.....	
8,000	8,000	April 1	Force	
.....	
.....	
.....	
10,000	9,000	May 1	75 days	Contract	
15,000	14,100	June 15	Oct. 15	Contract	
10,000	9,000	May 15	60 days	Contract	
10,000	9,800	May 1	30 days	Force	

CITIES —
WORK NOT STAR

City	Nature of Work	Location
Niagara Falls.	Paving	Perry ave. from Portage road to 20th st.....
Niagara Falls.	Paving	Fort st. from 16th st. to Portage road.....
Niagara Falls.	Paving	Alley bet. 12th and 13th sts..
Niagara Falls.	Paving	Alley bet. Main and 8th sts..
Niagara Falls.	Paving	Alley bet. 4th st. and Park place
Niagara Falls.	Paving	Alley bet. 5th and 6th sts....
Niagara Falls.	Paving	Alley bet. 4th and 5th sts....
Niagara Falls.	Paving	State st. from Ontario to Lockport st.....
Norwich
No. Tonawanda	Water works intake.....	Niagara river and Little Island
Newburgh
New Rochelle.
Olean
Oneida	Brick paving.....	Central ave.....
Oneida	Concrete paving.....	Pleasant ave.....
Oneida	Concrete paving.....	Linden st.....
Oneida	Brick paving.....	James st.....
Oneida	Brick paving.....	Broad st.....
Oneida	Brick paving.....	Lenox ave.....
Oneonta	Concrete culvert.....	Rose ave.....
Ogdensburg
Oswego
Poughkeepsie .	Water mains.....	Cedar st.....
Poughkeepsie .	Sewers	Howard and Hudson sts. and Fallkill ave.....
Poughkeepsie .	Installing electric pumping unit	City water plant.....
Plattsburg
Port Jervis
Rochester	Comfort station	East side
Rochester	Fire house	N. W. section.....
Rochester	Fire house	N. E. section.....
Rochester	Stables	Exposition park
Rochester	Bath house	South ave.....
Rochester	Bath house	North ave.....
Rochester	Bath house	Charlotte on Lake Shore....
Rochester	Municipal Hospital	Waring rd.
Rochester	Recreation building and bath house	West side

*Continued***TED — Continued**

Moneys Available	Estimated Cost of Construction	Date Work Will Start		Estimated Date of Completion	Contract or Force Account	Remarks
\$40,405	\$40,405	June	15	100 days	Contract	
9,700	9,700	May	1	30 days	Contract	
8,000	8,000	May	1	40 days	Contract	
5,700	5,700	July	1	30 days	Contract	
4,400	4,400	July	1	20 days	Contract	
22,000	22,000	July	1	60 days	Contract	
19,000	19,000	July	1	60 days	Contract	
47,000	47,000	July	1	60 days	Contract	
<u>\$201,205</u>	<u>\$198,105</u>					
.....					
\$80,000	\$77,000	May	15	90 days	Contract	
.....					
.....					
12,900	12,180	June	10	Contract	
2,400	2,296	June	10	Contract	
13,500	9,940	June	10	Contract	
6,908	6,908	May	26	Contract	
13,065	13,065	June	10	Contract	
33,000	32,954	May	26	Contract	
<u>\$81,773</u>	<u>\$77,343</u>					
\$1,200	\$1,200	June	1	30 days	Force	
.....					
5,400	5,400	March	6	1 month	Force	
6,000	6,000	March	5	80 days	Force	
32,000	32,000	April	1	140 days	Contract and Force	
<u>\$43,400</u>	<u>\$43,400</u>					
.....					
\$50,000	\$ 50,000	July	1	180 days	Contract	
40,000	40,000	June	1	150 days	Contract	
40,000	40,000	June	1	150 days	Contract	
28,000	28,000	April	1	120 days	Contract	
50,000	50,000	April	15	150 days	Contract	
30,000	30,000	May	15	150 days	Contract	
75,000	75,000	June	1	150 days	Contract	
125,000	125,000	May	1	180 days	Contract	
100,000	100,000	July	1	200 days	Contract	

CITIES —

WORK NOT STAR

City	Nature of Work	Location
Rochester	Comfort station	West side
Rochester	Grading and paving	Clarissa st.
Rochester	Pavement	
Rochester	Sewers	
Rome	Pavement and sewer	North Jay st.
Rome	Pavement and sewer	North George st.
Rome	Engine house	Ridge st.
Rensselaer		
Schenectady	Concrete tile sewers	Old Erie canal
Schenectady	Asphalt streets	Union st., North terrace, Glenwood boulevard
Schenectady	Paving with asphalt	Crane st.
Sherrill	Macadam street	Cottage place
Saratoga		
Syracuse	School house	6th ward, Prescott school
Syracuse	Addition to school house	5th ward, Lincoln school
Syracuse	School house	3d ward, Franklin school
Syracuse	Pavement	E. Willow, Lodi, Highland
Syracuse	Pavement	Tracy st., Plum to Van Rensselaer
Syracuse	Pavement	Leavenworth ave., Tracy to Wilkinson
Syracuse	Pavement	Bear st., N. Salina to Sunset ave.
Syracuse	Pavement	Dorset rd., Berkley to Stratford st.
Syracuse	Resurfacing pavement	Seymour st., Oswego to S. West st.
Syracuse	Resurfacing pavement	S. West st., Gifford to Shonard
Syracuse	Resurfacing pavement	Liberty st., Park ave. to W. Genesee st.
Syracuse	Resurfacing pavement	W. Genesee st., Liberty st. to Erie canal
Syracuse	Resurfacing pavement	Walton st., Onondaga creek to S. West st.
Syracuse	Resurfacing pavement	McBride st., Laurel to Butternut
Syracuse	Resurfacing pavement	E. Fayette st., Warren to Montgomery
Syracuse	Resurfacing pavement	W. Genesee st., Salina to S. West st.
Syracuse	Sewer	Kensington rd., Lancaster to 140 ft. W.
Syracuse	Sewer	Comstock pl. and Ostrom ave.

*Continued***TED — Continued**

Moneys Available	Estimated Cost of Construction	Date Work Will Start	Estimated Date of Completion	Contract or Force Account	Remarks
\$50,000	\$50,000	July 1	180 days	Contract	
45,000	45,000	April 15	120 days	Contract	
174,000	174,000	Contract	
179,000	179,000	Contract	
\$986,000	\$986,000				
\$25,000	\$25,000	June 1	Contract	
22,000	22,000	June 1	150 days	Contract	
9,000	9,000	Contract	
\$56,000	\$56,000				
.....				
\$19,000	\$19,000	50 days	Contract	
35,000	35,000				
18,000	18,000	30 days	
\$72,000	\$72,000				
\$1,600	\$1,600	April 15	10 days	Contract	
.....				
65,000	308,000	April 15	415 days	Contract	
60,000	297,500	May 1	400 days	Contract	
48,000	495,000	May 15	500 days	Contract	
20,000	20,000	May 1	60 days	Contract	
33,180	33,180	May 1	90 days	Contract	
4,700	4,700	June 1	30 days	Contract	
18,000	18,000	June 1	90 days	Contract	
9,000	9,000	May 1	30 days	Contract	
14,720	14,720	May 1	60 days	Contract	
18,000	18,000	May 1	75 days	Contract	
2,800	2,800	May 1	30 days	Contract	
29,460	29,460	May 1	120 days	Contract	
11,010	11,010	June 1	60 days	Contract	
3,500	3,500	June 1	30 days	Contract	
5,500	5,500	May 1	30 days	Contract	
38,000	38,000	120 days	Contract	
500	500	Aug. 1	30 days	Contract	
1,550	2,000	30 days	Contract	

**CITIES —
WORK NOT STAR**

City	Nature of Work	Location
Syracuse	Sewer	Grand ave. et al.....
Syracuse	Sewer	Spencer st. et al.....
Syracuse	Sewer	17th ward, west section.....
Syracuse	Sewer	17th ward, east section.....
Syracuse	Cement sidewalks	Various parts of city.....
Salamanca
Troy	Paving — bitulithic	1st st., Ferry st. to River st..
Troy	Paving — Granite block	Hoosick st.
Troy	Improving park, grading and sewering	Frear park
Troy	Paving and curbing.....	Vanderburg ave.....
Tonawanda ..	Extension of water mains....	William and Minerva sts.....
Utica	Paving	Various streets
Watervliet
Watertown ...	Grade crossing elimination...	Court st.
Watertown ...	Hydro-electric development...	Pumping station
White Plains .	Covering brook	Davis brook
White Plains .	Storm water sewer.....	Waller and Mamaroneck aves.
White Plains .	Repaving	Martine ave., etc.....
White Plains .	Repaving	Main st.....
GRAND TOTAL		

*Continued**TED — Concluded*

Moneys Available	Estimated Cost of Construction	Date Work Will Start	Estimated Date of Completion	Contract or Force Account	Remarks
\$20,300	\$25,000	150 days	Contract	Have been unable to get contractor for all of work.
4,400	6,000	90 days	Contract	
100,000	130,000	Now — on part	Contract	
200,000	250,000	Now — on part	Contract	
26,000	26,900	May 1	90 days	Contract	
<u>\$733,620</u>	<u>\$1,748,770</u>				
.....				
\$37,000	\$37,000	June 1	Oct. 1	Contract	
48,000	48,000	June 1	Nov. 1	Contract	
100,000	100,000	May 15	Nov. 1	Contract	
42,000	42,000	May 15	Oct. 15	Contract	
<u>\$227,000</u>	<u>\$227,000</u>				
\$8,000	\$7,000	June 1	Aug. 1	Contract	
180,000	180,000	Apr. 15	Nov. 1	Contract	
.....				
120,000	250,000	May 1	One year	Contract	City and State appropriation ready. Railroad appropriation has been approved but money has not been made available.
170,000	300,000	April 1	Two years	Water Board	
<u>\$290,000</u>	<u>\$550,000</u>				
\$8,500	\$25,000	Contract	Part of work may be done this year.
6,500	6,075	April 1	90 days	Contract	
20,000	20,000	Contract	
16,000	20,000	Contract	
<u>\$51,000</u>	<u>\$71,075</u>				
<u>\$4,367,796</u>	<u>\$5,779,911</u>				

CITIES —

WORK CON

City	Nature of Work	Location
Albany	Granite pavement and concrete walks	Central ave., Quail st. to Watervliet ave.....
Albany	Paving, curbing and walks...	Broadway, Pleasant st. to N. city line
Albany	Asphalt pavement and curbing	Western ave., from Manning boul. to W. city line.....
Amsterdam
Auburn	Paving	Clark st., from Monroe st. to Aurelius ave.....
Auburn	Paving	John st., Genesee st. to Franklin st.
Auburn	Paving	Grover st., South st. to Osborne st.
Auburn	Paving	Orchard st., James st. to So. Division st.
Auburn	Paving	Swift st., South st. to Lake ave.
Auburn	Paving	Seymour st., Washington st. to N. Division st.....
Batavia
Beacon
Buffalo
Binghamton ..	Concrete retaining wall.....	Various points on Pierce, Park and Chamberlain creeks....
Binghamton ..	Sanitary and storm sewer....	Brandywine creek channel....
Canandaigua
Cortland	Sewer	Williams st., south Church st.
Cohoes
Corning
Dunkirk
Elmira	Reinforced concrete bridge...	Main st.
Fulton
Glen Cove
Geneva

*Continued***TEMPLATED**

Estimated Cost of Construction	Date Work Will Start	Estimated Date of Completion	Contract or Force Account	Remarks
\$145, 000	June	140 days	Contract	Waiting for an enabling bill.
143, 040	June	120 days	Contract	Waiting for an enabling bill.
130, 000	May or June	160 days	Contract	
<u>\$418, 040</u>				
.....	
\$20, 000	180 days	Contract	
5, 300	30 days	Contract	
14, 000	60 days	Contract	
33, 000	July 1	90 days	Contract	
31, 000	80 days	Contract	
19, 700	July 1	90 days	Contract	
<u>\$123, 000</u>				
.....	
.....	
.....	
\$25, 000	May 15	100 days	Force	This is only a small part of the work deemed necessary. Total cost will be \$500,000.
200, 000	400 days	Contract	This work considered very necessary. Doubtful whether appropriation will be made.
<u>\$225, 000</u>				
.....	
\$2, 250	August	Force	
.....	
.....	
250, 000	Contract	
.....	
.....	

CITIES — **WORK CONTEMPL**

City	Nature of Work	Location
Gloversville ..	Surface water sewer.....	N. Main st. and W. 11th ave.
Gloversville ..	Bitulithic pavement	Bleecker st.
Gloversville ..	Reinforced concrete pavement.	E. Fulton st.
Gloversville ..	Reinforced concrete pavement.	N. Main st.
Glens Falls ...		
Hudson		
Hornell		
Ithaca		
Jamestown ...	Storm and sanitary sewers...	S. Main st., Martin rd. and Cole ave.
Johnstown		
Kingston		
Little Falls ...	Paving	
Lockport	Concrete highway	West Jackson st.
Lockport	Brick highway	Gooding st.
Lockport	Concrete highway	Benley parkway and Living- ston place.....
Lockport	Brick highway	Grand st.
Lockport	Concrete highway	Park ave.
Lockport	Asphalt block pavement.....	Pine st.
Lackawanna ..		
Mechanicville ..	Water, paving and repairs...	
Middletown ..	School house	Linden ave.
Middletown ..	Victory building	
Middletown ..	Sewage disposal plant and connecting sewer	One-half mile south of Mid- dletown
Middletown ..	Opening new street.....	Bet. King and W. Main sts..
Mt. Vernon...	Repaving street — asphalt block	No. and So. Columbus ave... Sugar st. from Walnut ave. to College ave.....
Niagara Falls.	Water main extensions.....	24th st. from La Salle ave. to Ontario ave.....
Niagara Falls.	Trunk sewer.....	27th st. from Niagara st. to Michigan ave.....
Niagara Falls.	Trunk sewer.....	Sugar st. from Central Court to Seneca ave.....
Niagara Falls.	Water main.....	Columbus ave. and Erie R. R. Co.....

*Continued***ATED — Continued**

Estimated Cost or Construction	Date Work Will Start		Estimated Date of Completion	Contract or Force Account	Remarks
\$12,600	May	15	60 days	Contract	
10,800	May	15	50 days	Contract	
28,000	May	1	120 days	Contract	
19,600	May	1	100 days	Contract	
<hr/>					
\$71,000					
<hr/>					
.....					
.....					
.....					
.....					
\$5,628		30 days	Contract	Work now being done.
.....					
.....					
100,000		two years	Contract	
18,300	June	1	30 days	Contract	
45,200	June	1	40 days	Contract	
13,000	July	1	20 days	Contract	
4,000	June	1	15 days	Contract	
50,000	July	1	50 days	Contract	
93,000	July	1	60 days	Contract	
<hr/>					
\$223,500					
<hr/>					
.....					
\$200,000		One year	Contract	
150,000	June or July		One year	Contract	
200,000		One year	Contract	
100,000		8 months	Contract	Work is held up because of failure of State to make appropriation for its share of cost.
10,000		4 months	Force	
<hr/>					
\$460,000					
<hr/>					
\$198,000	Contract	
140,000	June	15	200 days	Contract	
99,700	July	1	120 days	Contract	
113,100	July	1	160 days	Contract	
239,000	July	1	200 days	Contract	
68,100	July	1	250 days	Contract	
<hr/>					
\$659,900					

CITIES —
WORK CONTEMPL

City	Nature of Work	Location
Norwich
No. Tonawanda
Newburgh	Additional water supply.....
New Rochelle.	Sewers, drains, roads, etc....
Olean	Concrete bridge and repair work
Olean	Brick pavements.....
Oneida
Oneonta	Bit. macadam pavement.....	Maple st.....
Oneonta	Bit. macadam pavement.....	Elm st.....
Oneonta	Concrete side walks.....
Ogdensburg ..	Brick central fire station and concrete paving.....	Centre of business section....
Oswego	Concrete highways.....	Approaches to city of Oswego and State Normal School..
Poughkeepsie
Plattsburgh ..	Grading grounds, construction of walks, etc.....
Rochester	Pavement construction	Different sections of city....
Rochester	Sewer construction	Different sections of city....
Rochester	Sewer and walk construction.	Different sections of city....
Rochester	Pavement construction	Different sections of city....
Rochester	Two sewage disposal plants..	10th ward and 23d ward.....
Rochester	Water pipe extension.....	Crossing Genesee river at Mc- Lean pl.
Rochester	Primary School No. 31.....	Goodman st., near Circle st..
Rochester	Addition to School No. 37...	Post and Congress aves.....
Rochester	Madison Junior High School..	Bronson ave. and Wilson park.
Rochester	Monroe Junior High School..	Monroe ave. near Alexander st.
Rome	School house	Linden st.
Rensselaer ...	Repaving — granite blocks...	Broadway
Rensselaer ...	Repairs to jail and City Build- ing	Broadway, foot of John st....
Rensselaer ...	Repairs to fire alarm system..

*Continued**ATED — Continued*

Estimated Cost of Construction	Date Work Will Start	Estimated Date of Completion	Contract or Force Account	Remarks
.....				
\$525,000	Contract	Consent of Conservation Commission.
100,000	May 1	6 months	Contract and Force	
6,000	June 15	60 days	Undeter- mined	
125,700	May 1	200 days	Contract	
<u>\$131,700</u>				
.....				
\$27,845	May 1	130 days	
45,000	May 1	160 days	
10,000	Aug. 1	120 days	
<u>\$82,845</u>				
.....				
\$50,000	July 1	4 months	Contract	
175,000	May 1	180 days	Contract and Force	\$100,000 brings city to limit of its bonded indebtedness; \$75,000 needed through State and government aid.
.....				
25,000	
172,000	Contract	
43,600	Contract	
107,000	Contract	
88,000	Contract	
150,000	July 1	120 days	Contract	
50,000	July 1	90 days	Contract	
150,000	Aug. 1	300 days	Contract	
40,000	June 15	Sept. 15	Contract	
750,000	Oct. 1	480 days	Contract	
750,000	June 1	480 days	Contract	
<u>\$2,300,600</u>				
\$125,000	Contract	
125,000	Probably May	3 months	Contract	
4,000	April 15	30 days	Contract	
2,000	April	60 days	Contract	
<u>\$131,000</u>				

CITIES —
WORK CONTEMPL

City	Nature of Work	Location
Schenectady ..	Sewers — concrete	Eastern parkway, Palmer ave., Central Park
Schenectady ..	Sewers — tile.....	Livingston ave.
Schenectady ..	Sewers — tile.....	Union ave., University pl. to Wendell ave.
Schenectady ..	Paving, grading, taking down buildings	Erie canal, State st. to Union st.
Sherrill
Saratoga	Top dressing on gravel road..
Saratoga	Repairing water bound mac- adam
Syracuse	Fire house	8th ward
Syracuse	Improvement to parks.....
Syracuse	Repavement of street intersec- tion and public comfort sta- tion	Warren and Onondaga.....
Syracuse	Resurfacing highway	Park st.
Salamanca
Troy
Tonawanda ..	Street paving	William and Minerva sts....
Utica	Sewers
Watervliet
Watertown ...	Reinforced concrete bridge....	Factory st.
White Plains..
Yonkers	City Hall approach.....	City Hall
Yonkers	Regulating and grading.....	Glen park
GRAND TOTAL

*Continued***ATED — Concluded**

Estimated Cost of Construction	Date Work Will Start		Estimated Date of Completion	Contract or Force Account	Remarks
\$6,500		30 days	Contract	
1,700		15 days	Contract	
5,000		30 days	Contract	
57,065		60 days	Contract	
<u>\$70,265</u>					
.....					
\$3,500	June	1	5 to 6 weeks	Force	
10,960	June	1	6 weeks	Force	
<u>\$14,460</u>					
\$47,800	July	1	150 days	Contract	
75,000	May	1	200 days	Contract	
20,000	June	1	90 days	Contract	
16,000	June	1	30 days	Contract	
<u>\$158,800</u>					
\$55,000	
.....					
50,000	July	1	120 days	Contract	
30,000	June	1	Oct. 15	Contract	
.....					
60,000	June	1	5 months	Contract	
.....					
20,000	May	1	120 days	Contract	
15,000	April	15	90 days	Contract and Force	
<u>\$35,000</u>					
<u><u>\$7,055,988</u></u>					

CITY OF NEW YORK

NAME OF DEPARTMENT	WORK IN PROGRESS		WORK NOT STARTED		WORK CONTEMPLATED
	Moneys Available	Estimated Cost of Construction	Moneys Available	Estimated Cost of Construction	Estimated Cost of Construction
Armory Board	\$25,500	\$25,500	\$3,500
Bellevue and Allied Hospitals	90,000	80,000	1,967,000
Borough President—Manhattan	\$536,020	188,550	2,464,325	2,464,325	1,403,140
Borough President—The Bronx	1,746,400	1,578,800	2,613,755	2,613,755	2,369,672
Borough President—Brooklyn	3,347,863	3,347,863	2,540,600
Borough President—Queens	700,353	700,353	3,157,360
Borough President—Richmond	309,990	309,990	246,291
Correction
Docks and Ferries
Education	8,346,945	8,346,945
Fire
Health
Inebriety, Board of
New York Zoological Society	100,000	140,000	5,000
Parks, Manhattan and Richmond
Parks, The Bronx
Parks, Brooklyn
Parks, Queens
Plant and Structures
Police
Public Charities
Public Markets
Street Cleaning
Water Supply, Gas and Electricity
Totals	\$2,282,420	\$1,767,350	\$17,968,731	\$18,028,731	\$11,692,563
GRAND TOTALS	\$20,271,151	\$31,488,644
Public Service Commission (Rapid Transit Construction)	\$20,000,000	\$20,000,000	\$25,000,000	\$25,000,000	\$10,000,000
Board of Water Supply	12,138,738	12,138,738	12,000,000	12,000,000

YC 104853

Gaylamount
Pamphlet
Binder
Gaylord Bros., Inc.
Stockton, Calif.
T. M. Reg. U. S. Pat. Off.

UNIVERSITY OF CALIF. LIBRARY
JUN 2 1950
INTERLIBRARY LOAN

965
JA24
N7A5
F CALIFORNIA LIBRARY

